BRUHAT BENGALURU

Clients Name	Executive Engineer Byatarayanapura Division
Project Name	Package - 7, Including 2 Works of Rs. 210.00 Lakhs (1) PROVIDING AND FIXING WOODEN F STADIUM, VIDYARANYAPURA IN WARD NO. 09 (VIDYARANYAPURA), VIDYARANYA WARD NO. 10 (DODDABOMMASANDRA), VIDYARANYAPURA SUB DIVISION
Consultants	Rudraprasad Consultants
Project Manager /Team Leader	Karthik Rochan
Project Start Date	21-Jun-18
Project End Date	15-Dec-18
Project Length in Months	6 months

Sl. No	Assignment	Unit	Bag Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Jun-18
1	Earthwork in surface excavation in ordinary soil for leveling and lowering the ground manually (other than foundation of buildings, culverts, roads drains and trenches of pipe line and cables) and removing the excavated stuff to a distance not exceeding 50m and lift up lift 1.5, excavated surface leveled and neatly dressed disposed earth to be leveled after breaking of clods and neatly dressed as per specifications Specification. and as per drawing and the directions of Engineer in-charge.	Cum	708.15	708.15	100	27-06-18	25-09-18	90	
2	Removing B.S.slab of Drain and stacking and as per drawing and the directions of Engineer in-charge	Sqm	188.12	188.12	100	27-06-18	25-09-18	90	
3	Removing and refixing stone slabs of drains and pointing in CM (1:3) and as per drawing and the directions of Engineer in-charge.	Sqm	226.84	226.84	100	28-06-18	27-09-18	91	
4	Providing granite slabs of selected quality roughly dressed havinf a size of 7.5 cms thick and fixed in cement mortar (1:6) including fixing curing etc.and as per drawing and the directions of Engineer in-charge.	Sqm	37.32	37.32	100	03-07-18	25-10-18	114	
5	Providing granite slabs of selected quality roughly dressed havinf a size of 10 cms thick and fixed in cement mortar (1:6) including fixing curing etc and as per drawing and the directions of Engineer in-charge	Sqm	150.05	150.05	100	03-07-18	26-10-18	115	
6	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2meters and an average lift upto 1.5 m, excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications and as per drawing and the directions of Engineer in-charge.	Cum	44.44	44.44	100	14-07-18	28-10-18	106	
7	Lead for disposal of earth shall be payable at Carriage rates (Lead & Lift) by mechanical means including loading and unloading up to 15kms and as per drawing and the directions of Engineer in-charge	Cum	809.33	809.33	100	27-06-18	30-11-18	156	
8	Providing,laying, spreading and compacting crushed stone aggregates of granite'trap' basalt to wet mix macadam specification including pre mixing the Material with water at OMC in mechanical mix plant carriage of mixed material by tipper to site, laying in uniform layers with paver in sub-base /base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per specifications and as per drawing and the directions of Engineer in-charge	Cum	45.47	45.47	100	16-07-18	29-10-18	105	

MAHANAGARA PALIKE

OORING, PLAY EQUIPMENT, MULTI PURPOSE GYM EQUIPMENTS, BADMITON COURT, TABLE TENNIS STAND, YOGA MATT AND OTHER FITTINGS AT INDOOR
RA SUB DIVISION. (2) IMPROVEMENTS TO BALANCE ROADS AND DRAINS AT CHAMUNDESHWARI LAYOUT, NANJAPPA LAYOUT AND SURROUNDING AREAS IN



For RUDRAPRASAD CONSULTAN

Partner. / s.

BRUHAT BENGALURU

Clients Name	Executive Engineer Byatarayanapura Division
Project Name	Package - 7, Including 2 Works of Rs. 210.00 Lakhs (1) PROVIDING AND FIXING WOODE STADIUM, VIDYARANYAPURA IN WARD NO. 09 (VIDYARANYAPURA), VIDYARAN WARD NO. 10 (DODDABOMMASANDRA), VIDYARANYAPURA SUB DIVISION
Consultants	Rudraprasad Consultants
Project Manager /Team Leader	Karthik Rechan
Project Start Date	23-Jun-18
Project End Date	15-Dec-18
Project Length in Months	6 months

Sl. No	Assignment	Unit	Boq Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Jun-18
9	Cleaning the existing WBM Road surface including removing of binding materials and other foreign matter with wire brushes and small picks sweeping with brooms or soft brushes and finally dusting with old gunny bags and bar or compressed air to receive bituminous treatment including cost of all materials, labhour, HOM of machineries complet as per specifications and as per drawing and the directions of Engineer in-charge.	Sqm	193.20	193.20	100	22-07-18	03-11-18	104	
10	Providing and applying tack coat using 80/100 grade bitumen (VG 10) on granular base such as WBM surface hot bitumen primed at 4kg per 10 sqm heating bitumen in boiler with spray set (Excluding cleaning of Road surface) inlcuding cost of all materials, labhour, HOM of machineries complete as per specifications and as per drawing and the directions of Engineer in-charge.	Sqm	193.20	193.20	100	24-07-18	04-11-18	103	
11	Providing and laying bituminous macadam on prepared surface with crushed coarse as per design mix formula for base : binding courseincluding loading of aggregates with F.E. loader, hot mixing of stone aggregates and bitumen in hot mix plant,transporting the mixed material in tipper to paver and laying mixed materials, with paver finisher to the required level and grade,rolling by power roller to achieve the desired density,but excluding cost of primer'tack coat including lead,lift and cost of all materials,labour,HOM of machineries complete as per specifications and as per drawing and the directions of Engineer in-charge.	Cum	36.32	36.32	100	24-07-18	04-11-18	103	
12	Cleaning the existing black topped surface with brooms,soft brushes and finally dusting with old gunny bags and/or compressed air to receive bituminous treatment including cost of all materials,labhour, HOM of machineries complete as per specifications and as per drawing and the directions of Engineer in-charge	Sqm	7031.62	7031.62	100	02-08-18	10-11-18	100	
13	Providing and applying tack coat using 80/100 grade bitumen(VG10) in boiler fitted with spray set distributor at the rate of 0.20kg per sqm on the existing prepared bituminous surface.	Sqm	7031.62	7031.62	100	07-08-18	17-11-18	102	
14	Providing and laying bituminous concrete using crushed aggregates of specified grading, as per MORTH specification and as per drawing and the directions of Engineer in-charge.	Cum	311.63	311.63	100	07-08-18	17-11-18	102	

MAHANAGARA PALIKE

FLOORING, PLAY EQUIPMENT, MULTI PURPOSE GYM EQUIPMENTS, BADMITON COURT, TABLE TENNIS STAND, YOGA MATT AND OTHER FITTINGS AT INDOOR
URA SUB DIVISION. (2) IMPROVEMENTS TO BALANCE ROADS AND DRAINS AT CHAMUNDESHWARI LAYOUT, NANJAPPA LAYOUT AND SURROUNDING AREAS IN

For RUDRAPRASAD CONSULTANTS

Partner./s.

BRUHAT BENGALURU

Clients Name	Executive Engineer Byatarayanapura Division
Project Name	Package - 7, Including 2 Works of Rs. 210.00 Lakhs (1) PROVIDING AND FIXING WOOD STADIUM, VIDYARANYAPURA IN WARD NO. 09 (VIDYARANYAPURA), VIDYARA WARD NO. 10 (DODDABOMMASANDRA) VIDYARANYAPURA SUB DIVISION.
Consultants	Rudraprasad Consultants
Project Manager /Team Leader	Karthik Roshan
Project Start Date	23-Jun-18
Project End Date	15-Dec-18
Project Length in Months	6 months

Sl. No	Assignment	Unit	Boq Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Jun-18
15	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface as per drawing and the directions of Engineer in-charge.	Sqm	137.16	137.16	100	10-11-18	15-12-18	35	
16	Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 cum in volume and stock piling at designated locations and disposal of dismantled materials stacking serviceable and unserviceable materials seperately complete as per specifications. and as per drawing and the directions of Engineer in-charge.	Cum	56.75	56.75	100	22-08-18	23-09-18	32	
17	Construction of dry lean cement concrete mix CC1:5:10 as per directions of Engineer in-charge	cum	56.75	56.75	100	05-09-18	10-10-18	35	
18	Cement concrete pavement Construction of un-reinforced plain cement concrete pavement, thickness as per design, over a prepared sub base with OPC cement or any other type as per clause 1051.2.2 design mix M20/M30 , with 25mm and down size graded granite metal coarse aggregates and fine aggregates , with superplastisiser @3lts confirming to IS9103-1999 Reaffirmed-2008 , mixed in a concrete mixer of not less than 0.6 cum capacity and appropriate weigh batcher as per approved mix design, laid in approved fixed side form work (steel channel, laying and fixing of 125 micron thick polythene film, wedges, steel plates including levelling the form work as per drawing).	cum	59.29	59.29	100	17-09-18	10-11-18	34	
19	Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms and 2Ltr of Primer per sqm area, thickness of 2.5 mm is exclusive of surface applied glass beads as per IRC:35. The finished surface to be level, uniform and free from streaks and holes complete as per specifications and as per drawing and the directions of Engineer in-charge.	Sqm	9.71	9.71	100	10-11-18	15-12-18	35	

Legends

MAHANAGARA PALIKE

ORDING PLAY EQUIPMENT, MULTI PURPOSE GYM EQUIPMENTS, BADMITON COURT, TABLE TENNIS STAND, YOGA MATT AND OTHER FITTINGS AT INDOOR
RA SUB DIVISION. (2) IMPROVEMENTS TO BALANCE ROADS AND DRAINS AT CHAMUNDESHWARI LAYOUT, NANJAPPA LAYOUT AND SURROUNDING AREAS IN

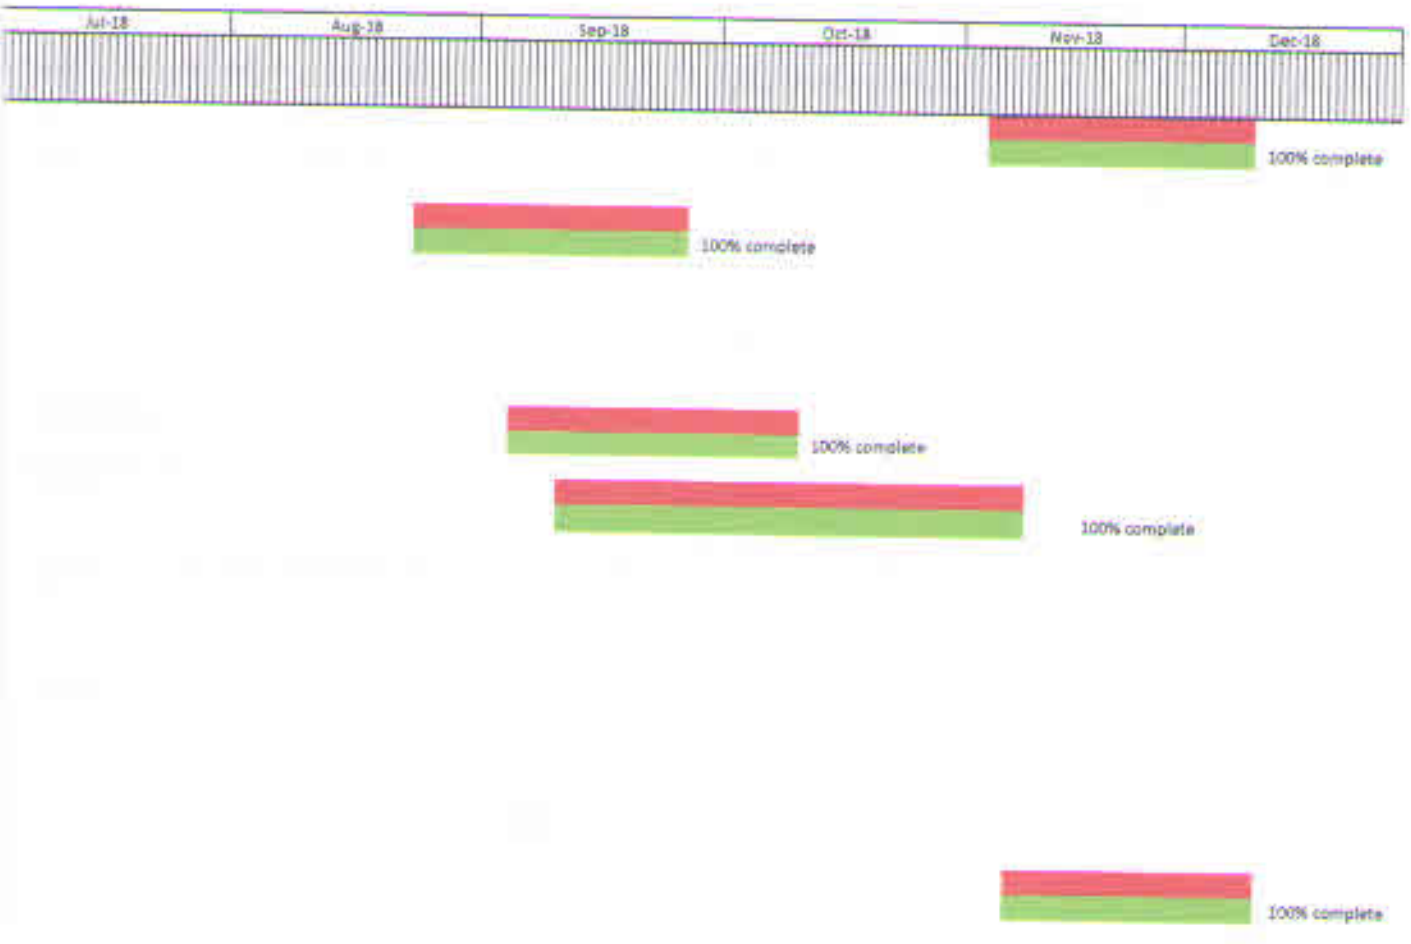

- Planned %
- Executed %

For RUDRAPRASAD CONSULTANTS

Partner./s.
